



existing

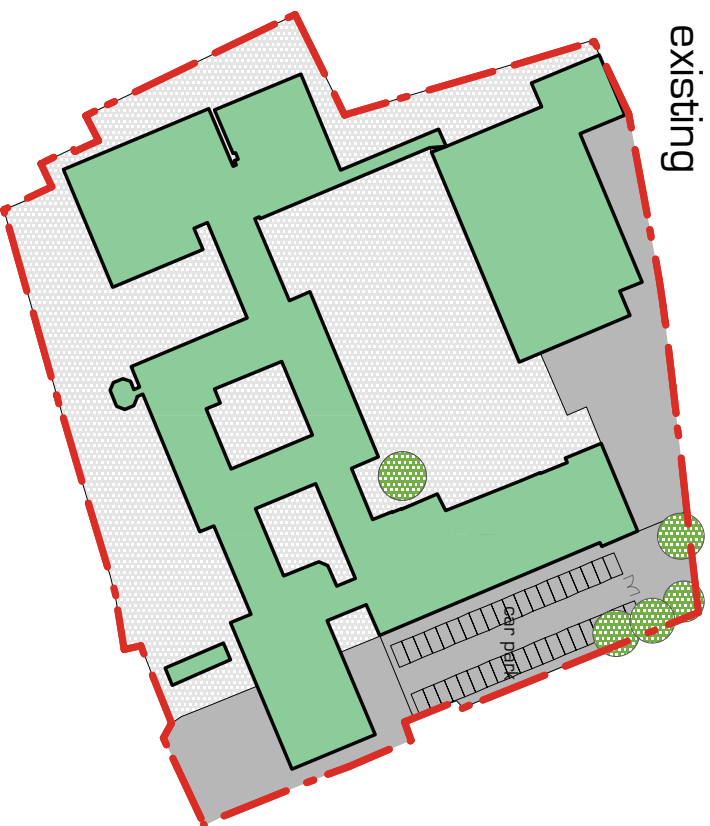


phase\_01

set up construction compound at front of school site protection to existing buildings complete new build main hall, admin and changing facilities breakthrough and connection made into existing building during 6 week summer break

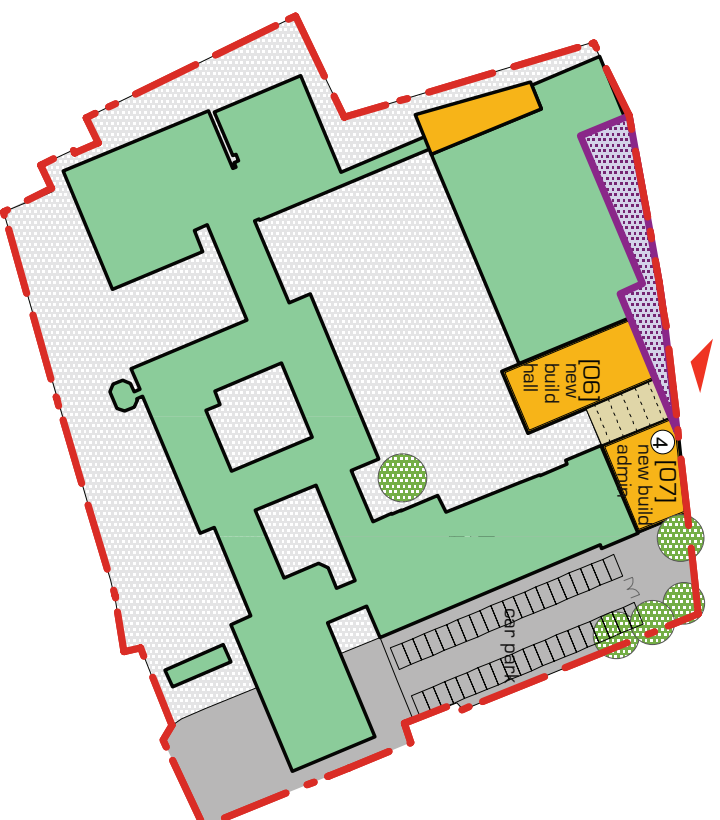


phase\_02

decent school admin, reception and main hall into completed new build. create new site compound as shown and demolish existing school buildings to create site for phase 2. build and complete phase 2 construction to provide 4 storey teaching facilities.

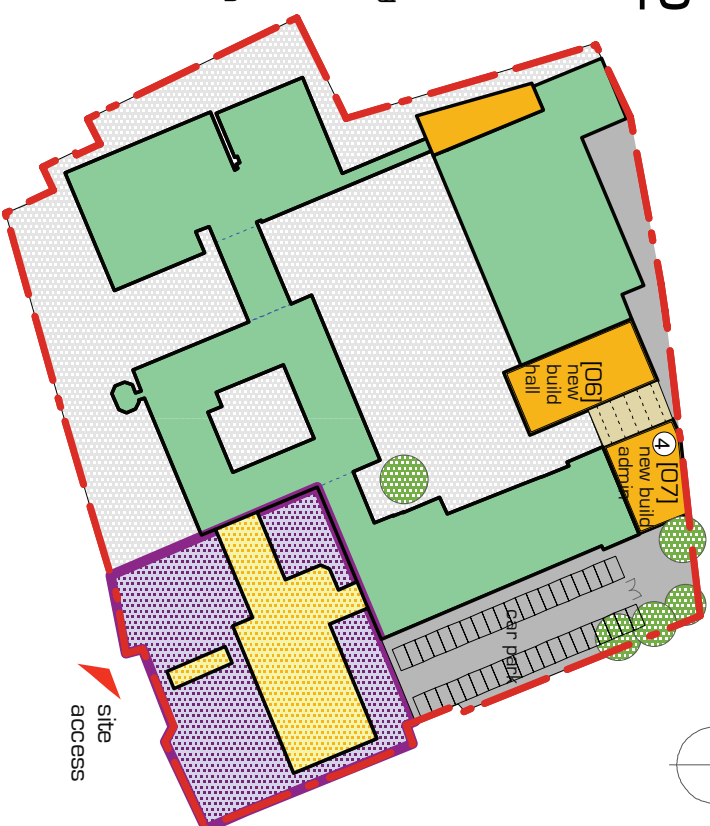


completed

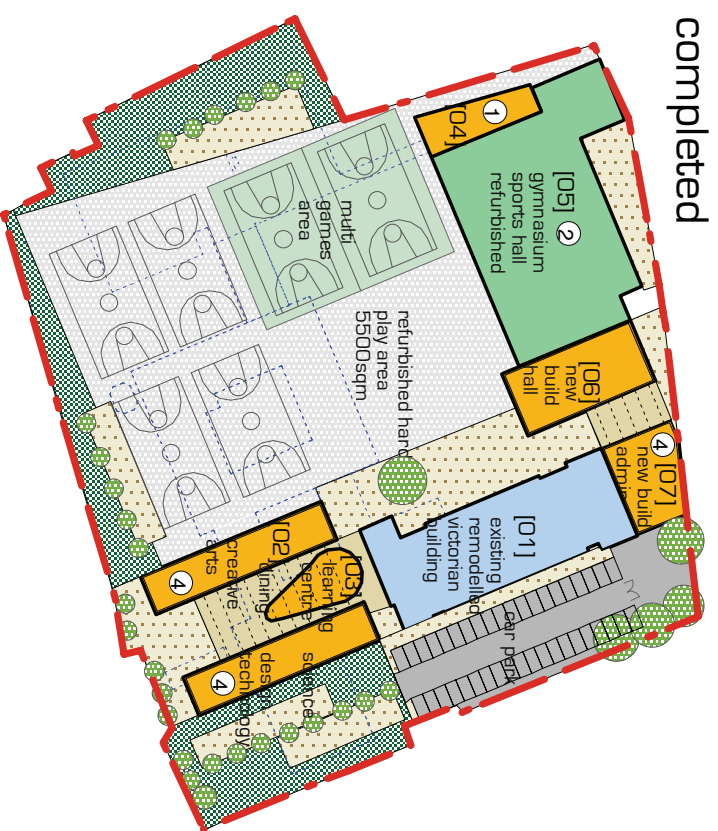


phase\_04

complete remodelling work within existing Victorian building and links into new build. (temporary accommodation maybe required dependant on build programme) complete landscaping works to remaining school site.

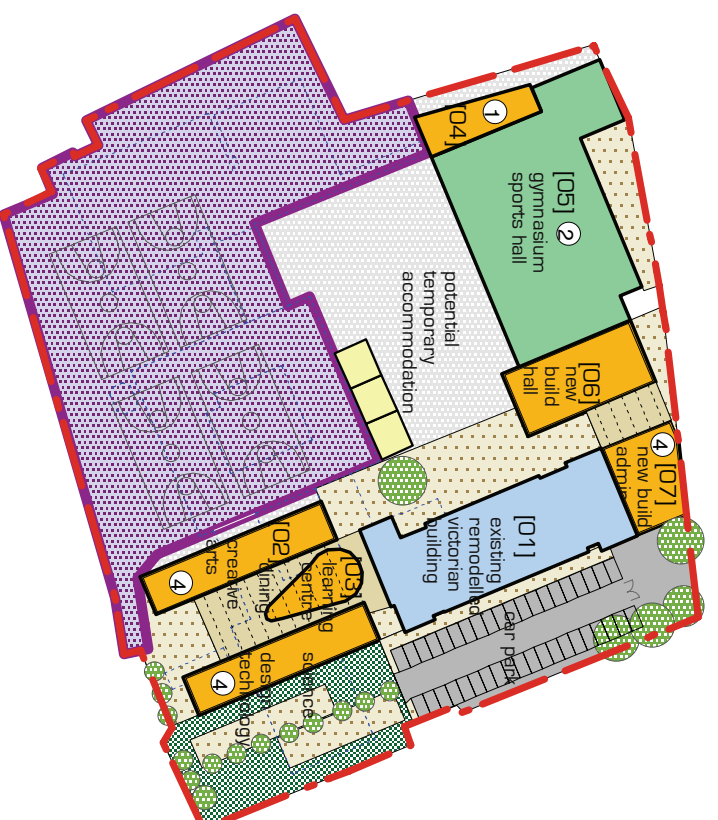

phase\_03

decent school department areas into new build accommodation to free up remaining buildings for demolition. demolish remaining existing buildings to provide site area for landscaping improvements.

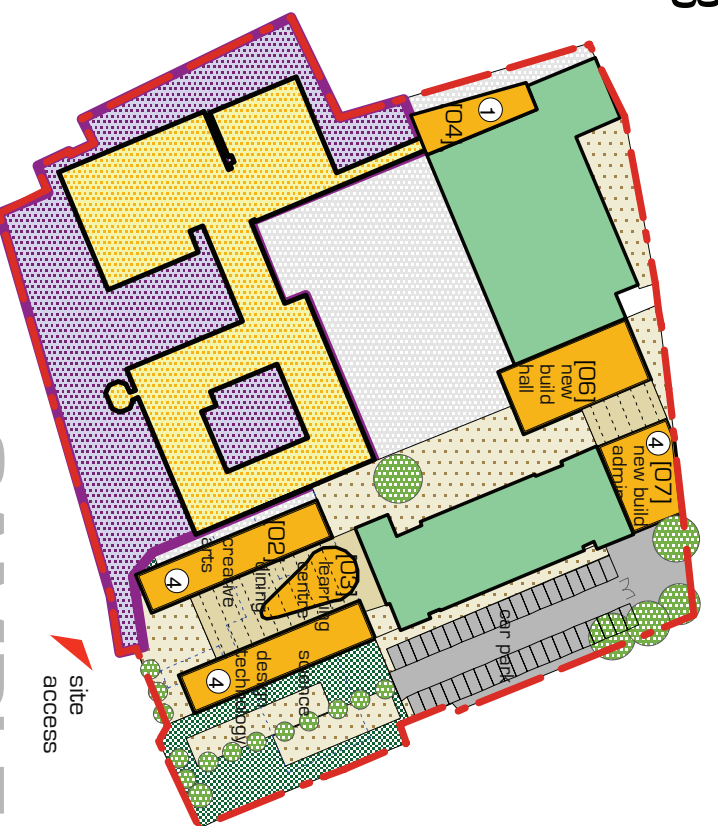

SAMPLE

construction site area buildings to be demolished

DRAWING PURPOSE

To show how the construction phases of the proposed works, taking account of decanting, refurbishment, demolition and new build.
